


Perry County Courthouse Weekly Summary

Updated 12/22/23



Scaffolding East Elevation 12/22/23

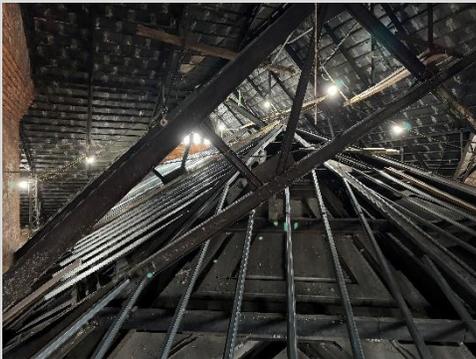

Hat Channel Install For Courtroom
Sheathing 12/22/23



Replicated Cast Iron Baluster Seen
Next To Existing 12/22/23

Construction Activities

- Ongoing Design Meetings
- East Elevation Scaffolding 100% Complete
- Hat Channel Installed Over Courtroom Ceiling. Plywood Sheathing To Start Next Week.
- O. K. Foundry Has Provided Replicated samples including Cast Iron Baluster And Ornaments For The Historical Staircase. Samples Have Been Shipped To Jobsite.

Total Manhours Worked To Date

- 5,763 Hours

Requests for Information (RFI's)

- None At This time

Submittals

- None At This Time

Weekly Weather Report

- Weather Did Not Affect Jobsite.

Cost Risk Exposure

- Schooley Caldwell Released Phase 2 Permit Bid Set 11/9/23. Initial Bids To CK Were Due On 12/15/23 From Potential Bidders. CK To Start Scope And Bid Reviews.
