


# Perry County Courthouse Weekly Summary

Updated 12/28/23



Plywood Sheathing Over Main Courtroom Ceiling 12/28/23

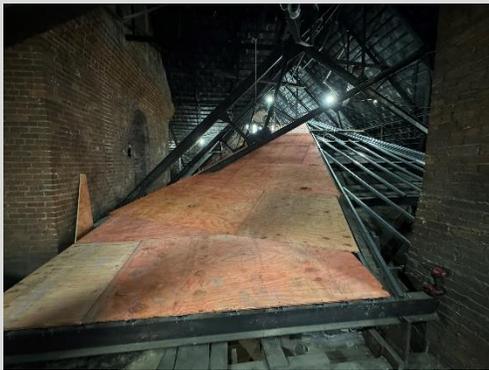

Large Newel Post Removed 12/28/23



Replicated Cast Iron Ornaments Next To Original Painted Ornaments 12/28/23

## Construction Activities

- Hat Channel Installation Complete Over Main Courtroom Ceiling. Structural Inspection Completed On 12/28/23.
- Ongoing Plywood Sheathing Over Main Courtroom Ceiling.
- Large Newel Post Removed And Ready For Replication.
- Replicated Cast Iron Ornaments Have Been Sent To Jobsite By O.K. Foundry.
- Propane Tank Delivered To Jobsite. Heaters To Be Installed Next Week.

## Total Manhours Worked To Date

- 5,891 Hours

## Requests for Information (RFI's)

- None At This time

## Submittals

- None At This Time

## Weekly Weather Report

- Weather Did Not Affect Jobsite.

## Cost Risk Exposure

- Schooley Caldwell Released Phase 2 Permit Bid Set 11/9/23. Initial Bids To CK Were Due On 12/15/23 From Potential Bidders. CK To Start Scope And Bid Reviews.
