

Perry County Courthouse Weekly Summary


Updated 3/8/24



South Elevation 3/8/24



South Elevation Stone Cleaning
3/8/24

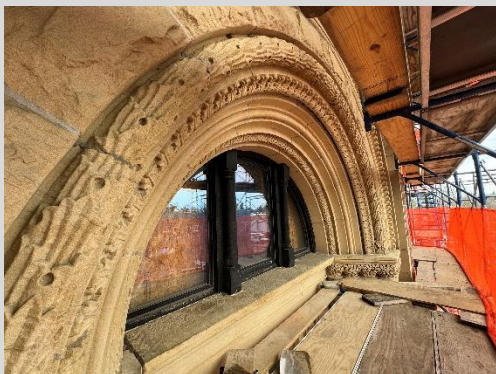

South Elevation Stone Cleaning
Mockup 3/8/24

Construction Activities

- Masons Completed South Elevation Stone Cleaning. Planning To Start On West Elevation Cleaning Next Week.
- Masons Created Stone Patching Samples For Accurate Color Comparisons.
- Window Supplier & Installer Field Measured Openings 3/7.
- Roofing Contractor Met Onsite 3/7 for Preconstruction Meeting. Planning To Mobilize Next Week.
- Scaffolding Contractor Installed Trash Chutes On North And South Elevations.

Total Manhours Worked To Date

- 8,251 Hours

Request For Information (RFI's)

- 028 - Roof Hat Channel
- 029 - Egress Door 018
- 030 - Existing Lightning Protection

Submittals

- 04 01 40.92 - PD for Masonry Patching Colors
- 04 01 40.92 - Mockup for Masonry Stone Patching

Weekly Weather Report

- No Weather Events Affected Work.

Cost Risk Exposure

- CK Continuously Reviewing Bids And Working Towards Providing Updated Costs For Owner Review. CK Working On GMP 2A Budgeting.
