


Perry County Courthouse Weekly Summary

Updated 3/29/24



New Roof Sheathing Seen From Attic
3/29/24

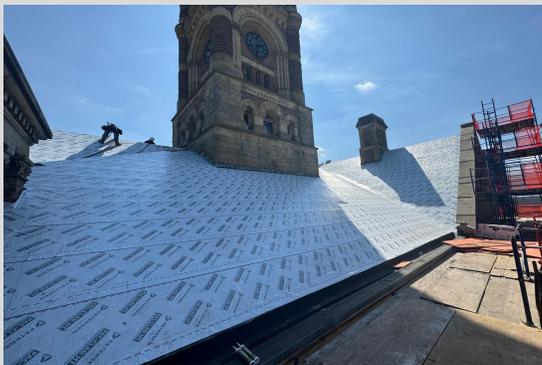

North Elevation Roof Sheathing
3/29/24



East Elevation Roof Sheathing
3/29/24

Construction Activities

- Masons Continued Working On Color Mockups For Design Team Review.
- Roofers Continued Removal Of The Existing On The North And East Elevations Of The Roof And Continued Install Of New Sheathing.
- Mays Consulting Reviewed New Roofing, and Masonry Conditions On North & West Elevations.
- Kokosing Surveying Group On-Site To Investigate Existing Downspouts, And Sanitary Lines.

Total Manhours Worked To Date

- 9,396 Hours

Request For Information (RFI's)

- 7 Open RFI's

Submittals

- 13 Open Submittals

Weekly Weather Report

- Rain And High Winds On 3/26 Prevented Masons And Roofers From Working.
- Expecting Stormy Weather Throughout Next Week.

Cost Risk Exposure

- CK Finalizing GMP-2A.
