


# Perry County Courthouse Weekly Summary


Updated 4/12/24



Scaffolding Bridge 4/12/24

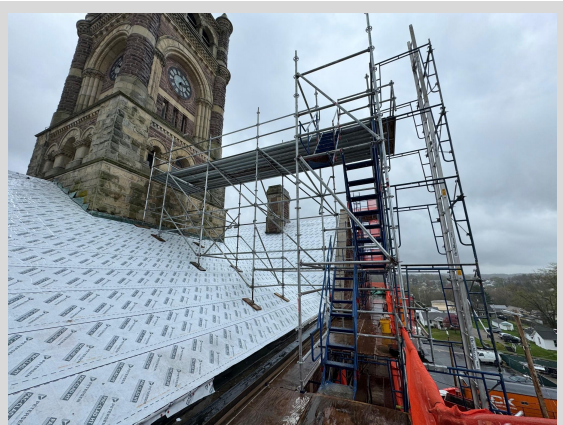

West Elevation Roofing 4/12/24

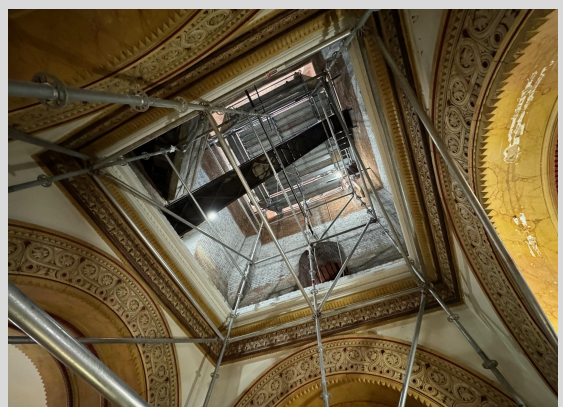

Interior Bell Tower Scaffolding 4/12/24

## Construction Activities

- Roofers Continued Removal And Installation Of New Roof Sheathing On The West Elevation Of The Roof.
- CK Laborers Grouted Attic Steel And Performed General Site Cleanup.
- CK Project Team Walked With The Design Team Reviewing Plans For Courthouse Main Entryway.
- Scaffolding Subcontractors Began Erection Of Bridge Connecting To The Bell Tower, And Interior Bell Tower Scaffolding

## Total Manhours Worked To Date

- 10,855.5 Hours

## Request For Information (RFI's)

- 6 Open RFI's

## Submittals

- 3 Open Submittals

## Weekly Weather Report

- Rainy Weather Prevented Roofers, Masons, And Scaffold Erectors From Working.
- Working Days Lost This Week: 3
- Rainy Weather Expected Mid Next Week.

## Cost Risk Exposure

- Perry County Commissioners Approved GMP-2A 4/10/24. CK Continued Working On Finalizing GMP-2B.
