


Perry County Courthouse Weekly Summary

Updated 4/19/24



East Tower Roofing 4/18/24

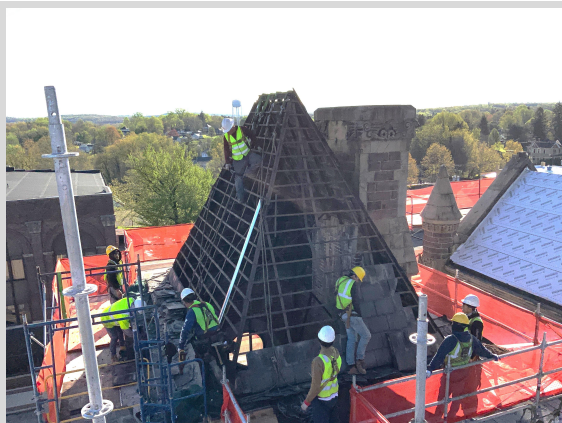

Install Of Bell Tower Structural
Scaffolding Base 4/19/24



Bell Tower Structural Scaffolding Base
4/19/24

Construction Activities

- Roofers Completed Removal And Installation Of New Roof Sheathing On The Main Portion Of The Roof This Week. Roofers Began And Will Continue Install Of New Roof Sheathing On The East Towers Next Week.
- Scaffolding Erectors Utilized A Crane To Install Beams Through Bell Tower Windows To Begin Tower Scaffolding.
- Masons Continued Mortar & Stone Patching Around The Building.
- CK Laborers Removed Existing Millwork On The 1st & 2nd Floor.

Total Manhours Worked To Date

- 11,790.5 Hours

Request For Information (RFI's)

- 6 Open RFI's

Submittals

- 3 Open Submittals

Weekly Weather Report

- Rainy Weather Prevented Roofers And Masons From Working.
- Working Days Lost This Week: 2
- Rainy Weather Expected Mid Next Week.

Cost Risk Exposure

- Perry County Commissioners Approved GMP-2A 4/10/24. CK Continued Working On Finalizing GMP-2B.
